ID	Task Mode	Task Name	Duration	Start	Finish
1		**New City Hall**	**184 days?**	**Tue 8/28/18**	**Fri 5/10/19**
2		**RFB Bid Approval**	**47 days**	**Tue 8/28/18**	**Wed 10/31/18**
3		Council Project Approval	0 days	Tue 8/28/18	Tue 8/28/18
4		Addv TNE & DJC	16 days	Wed 9/5/18	Wed 9/26/18
5		Pre-Bid meeting	0 days	Wed 9/12/18	Wed 9/12/18
6		Bid Due	0 days	Wed 9/26/18	Wed 9/26/18
7		Bid Review	6 days	Wed 9/26/18	Wed 10/3/18
8		PlanComm Action CU-ZC	0 days	Mon 10/15/18	Mon 10/15/18
9		PlanComm Wait Period	12 days	Tue 10/16/18	Wed 10/31/18
10		RCA	0 days	Thu 10/18/18	Thu 10/18/18
11		Council Award	0 days	Tue 10/23/18	Tue 10/23/18
12		Notice of Award	0 days	Wed 10/24/18	Wed 10/24/18
13		**Construction**	**122 days?**	**Wed 10/24/18**	**Thu 4/11/19**
14		Contract Administration	8 days	Wed 10/24/18	Fri 11/2/18
15		Notice to Proceed	0 days	Fri 11/2/18	Fri 11/2/18
16		Construction	75 days	Mon 11/5/18	Fri 2/15/19
17		Construction Time Extension	31 days?	Fri 2/15/19	Fri 3/29/19
18		Construction Final	10 days	Fri 3/29/19	Thu 4/11/19
19		**Liguidated Damages**	**21 days**	**Fri 4/12/19**	**Fri 5/10/19**
20		Liquidated Damages 1	11 days	Fri 4/12/19	Fri 4/26/19
21		Liquidated Damages 2	10 days	Sun 4/28/19	Fri 5/10/19
22		**Structural Permits**	**27 days**	**Mon 9/17/18**	**Tue 10/23/18**
23		Structural Permit Start	0 days	Mon 9/17/18	Mon 9/17/18
24		City Review 1	26 days	Tue 9/18/18	Tue 10/23/18
25		Permits Ready	0 days	Tue 10/23/18	Tue 10/23/18
26		Permits Issued	0 days	Tue 10/23/18	Tue 10/23/18
27		**MEP Deferred Submittals**	**78 days?**	**Wed 9/12/18**	**Fri 12/28/18**
28		MEP Pre-Lim Design	11 days	Wed 9/12/18	Wed 9/26/18
29		MEP Design	30 days?	Wed 10/24/18	Tue 12/4/18
30		MEP Deferred Permit Review	0 days	Tue 12/4/18	Tue 12/4/18
31		City Review 2	18 days	Wed 12/5/18	Fri 12/28/18
32		MEP Permits Ready	0 days	Fri 12/28/18	Fri 12/28/18
33		MEP Permits Issued	0 days	Fri 12/28/18	Fri 12/28/18

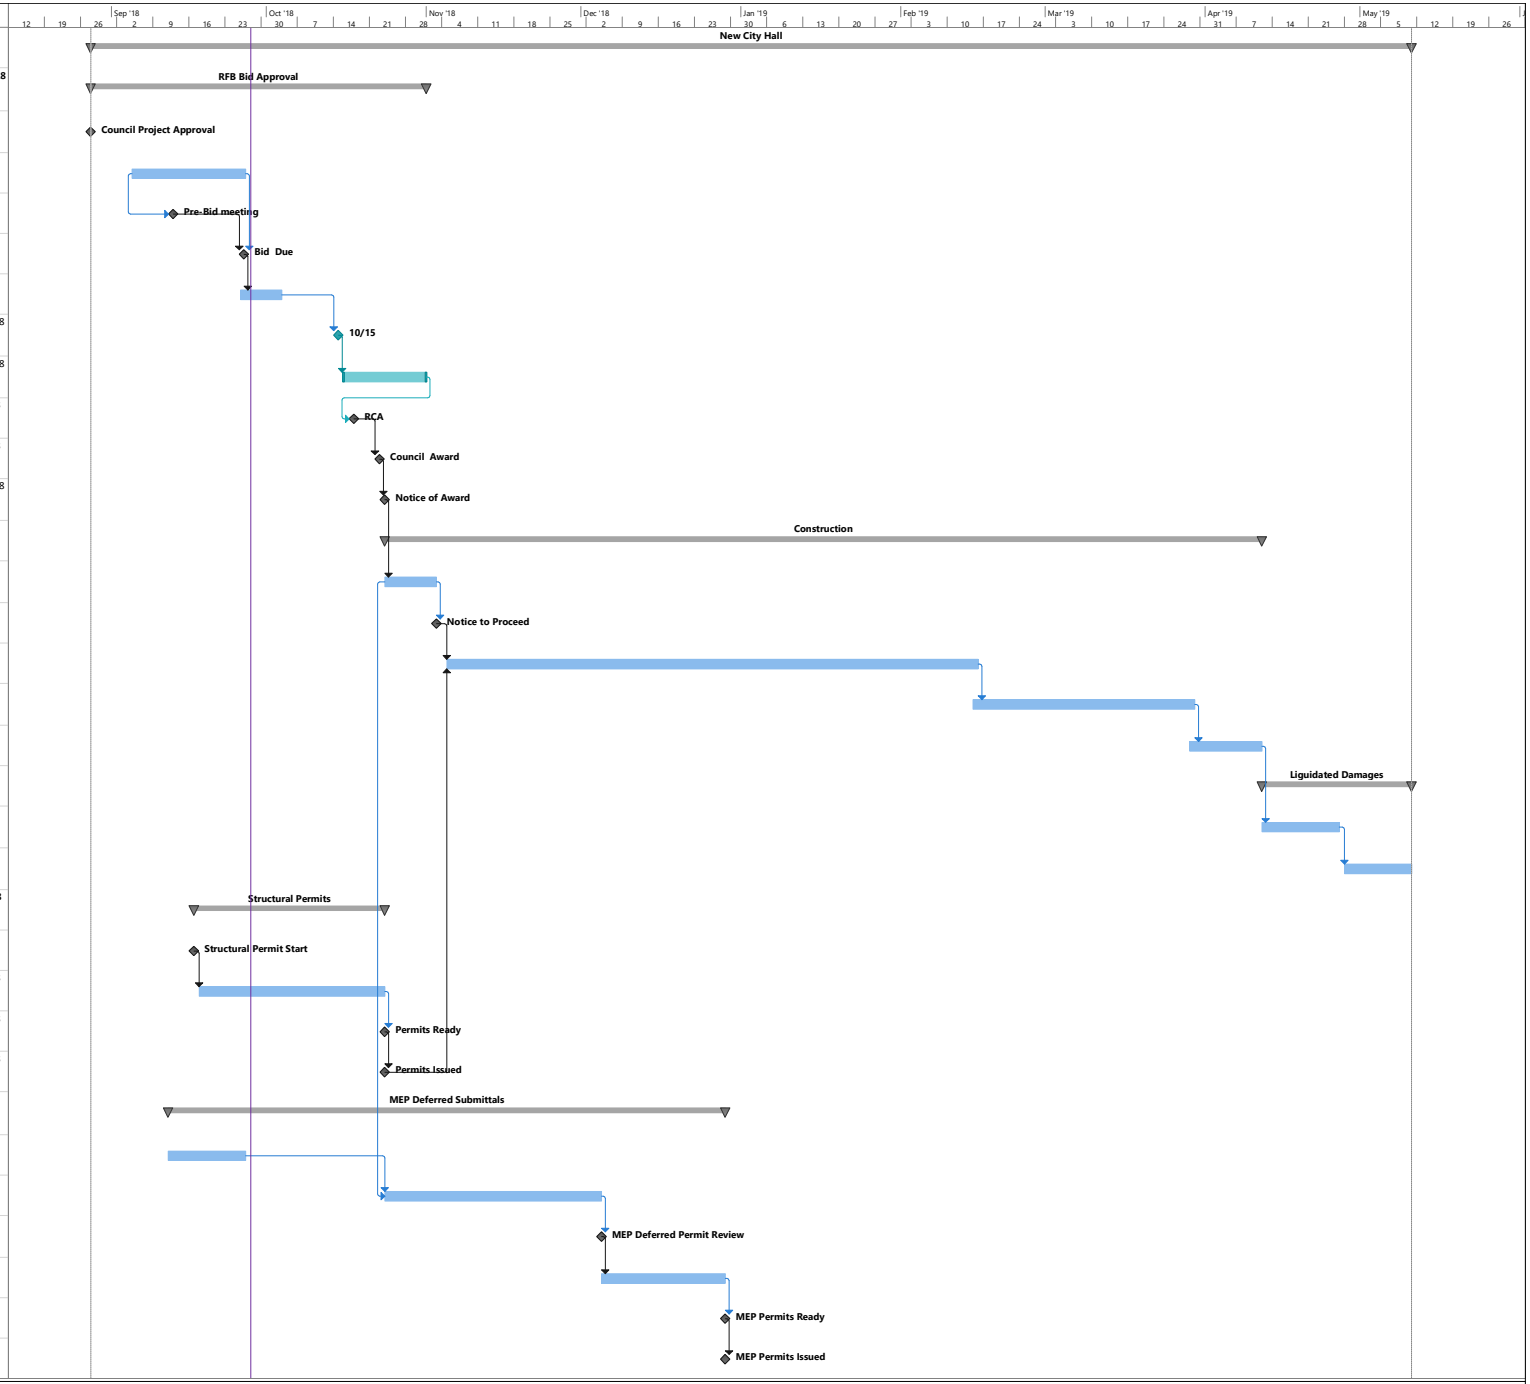

Project: City Hall Const Sched
Date: Fri 9/28/18

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
